

Homewood High – Phase 2: Interior Renovation

PROGRAM MANAGER: Hoar Program Management (HPM)
 ARCHITECT: Goodwyn Mills & Cawood (GMC)
 CONTRACTOR: MJ Harris Construction


SCOPE OVERVIEW:

Expanded Dinning, Serving & Kitchen Modifications, Repurposed Areas: Media Center (Collaboration Space/ Learning Hub), Interior Student Flow Improvements, Science Lab upgrades, weight room conversion.

CONTRACT RECAP:	Start	Executed CO	Projected Finish
• Contract Amount	\$3,819,100	0	08/2019
• Contract Schedule	01/2019	0	08/2019



Progress Status: Material Procurement

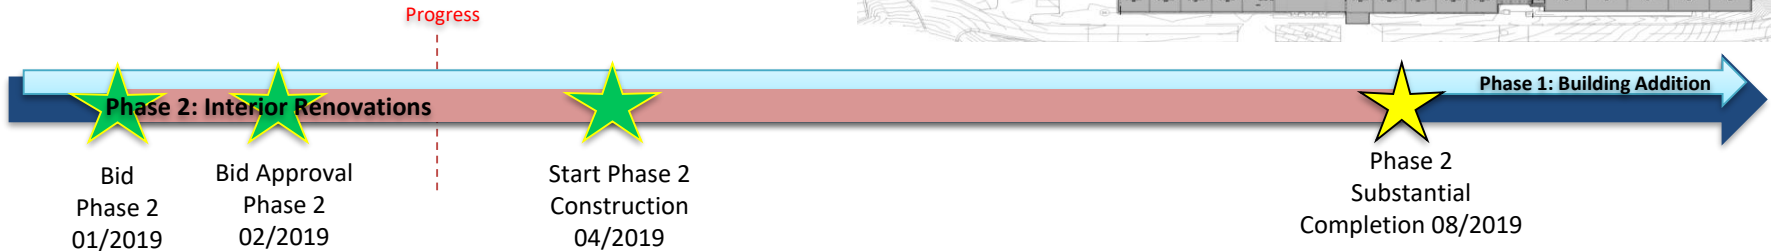

ACHIEVEMENTS:

- ✓ Advertise for Bid –Ph 2
- ✓ DD Budget Check - Ph 2
- ✓ CD/ Final Drawing Submittal - Ph 2
- ✓ CD/ Final Budget Check – Ph 2
- ✓ Phase 2 Bid Approval
- ✓ Notice of Award
- ✓ Notice to Proceed with Procurement

NEXT STEPS:

- Submittal & Shop Drawing Approvals
- Material Order Placements for Long Lead Items
- Begin Summer Phase work April 2019

CLOSURES & SHUTDOWNS:

- Science Pod Closure Relocation: Starting April 2019
- Kitchen Closure: Starting April 2019
- Bailey Theater Closure: Starting April 2019

