

Homewood High - Demolition

PROGRAM MANAGER: Hoar Program Management (HPM)
 ARCHITECT: Goodwyn Mills & Cawood (GMC)
 CONTRACTOR: Taylor & Miree Construction


SCOPE OVERVIEW:

Remove classroom / fine arts and athletic wings structures, re-establish utilities to remain in working condition for school year.

CONTRACT RECAP:	Start	Executed CO	Actual Finish
• Contract Amount	\$1,462,023	\$76,485	\$1,538,508
• Contract Schedule	June 5, 2018	0 Days	October 1, 2018



Progress Status: Substantially Complete

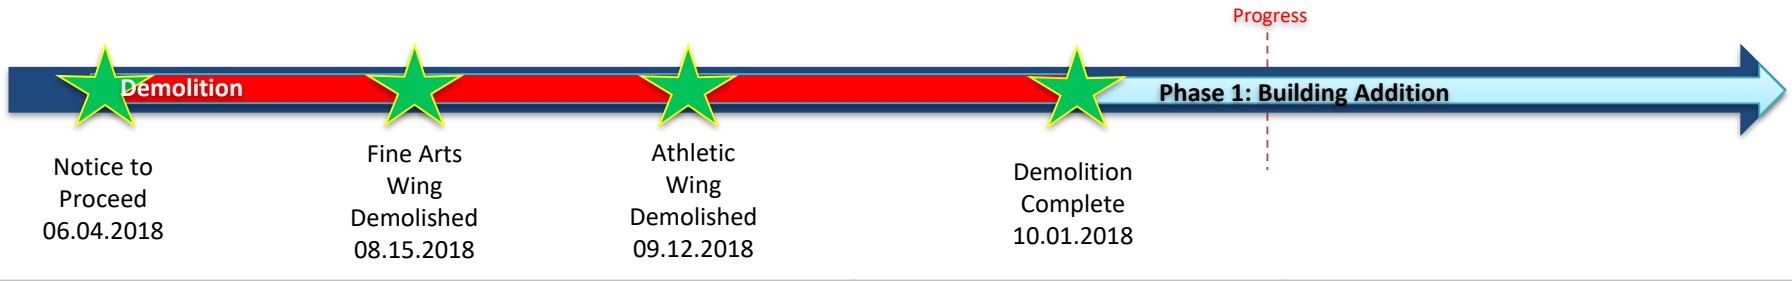

ACHIEVEMENTS:

- ✓ Demolish classroom / fine arts wing
- ✓ Demolish athletic wing
- ✓ Haul Off & Cleanup.
- ✓ State Inspection Sign Off
- ✓ Transition for Addition
- ✓ Demolition Substantial Completion

NEXT STEPS:

- Retain close-out documents

CLOSURES & SHUTDOWNS:

- N/A

